


Burbank Sanitary District
Baseline Schedule

ID	Task Name	Pipe ID	Duration	Start	Finish	Predecessor	September	October	November	December	January	February	March	April
1	#1004 - Burbank Sanitary District		110 days	Mon 10/4/21	Fri 3/4/22									
2	Notice to Proceed	-	1 day	Mon 10/4/21	Mon 10/4/21									
3	Submittals		5 days	Mon 10/4/21	Fri 10/8/21									
4	Clean & CCTV	-	10 days	Mon 10/11/21	Fri 10/22/21	3								
5	Liner Procurement	-	10 days	Mon 10/11/21	Fri 10/22/21									
6	CIPP Lining	-	38 days	Mon 10/25/21	Wed 12/15/21	5								
7	Cecil St	LU-103	1 day	Mon 10/25/21	Mon 10/25/21									
8	Cecil St	LU-104	0.5 days	Tue 10/26/21	Tue 10/26/21	7								
9	Cecil St	LU-104A	0.5 days	Tue 10/26/21	Tue 10/26/21	8								
10	Bascom Ave	HU-101	0.5 days	Wed 10/27/21	Wed 10/27/21	9								
11	Brookland Ave	LU-108A	1 day	Wed 10/27/21	Thu 10/28/21	10								
12	Brookland Ave	LU-108	1 day	Thu 10/28/21	Fri 10/29/21	11								
13	Boston Ave	LU-109	1 day	Fri 10/29/21	Mon 11/1/21	12								
14	Wabash Ave	LU-110	4.5 days	Mon 11/1/21	Fri 11/5/21	13								
15	Laswell Ave	LU-202	0.5 days	Mon 11/8/21	Mon 11/8/21	14								
16	Vaughn Ave	LU-205	0.5 days	Mon 11/8/21	Mon 11/8/21	15								
17	Arieta Ave	LU-208	0.5 days	Tue 11/9/21	Tue 11/9/21	16								
18	Arieta Ave	LU-209	1 day	Tue 11/9/21	Wed 11/10/21	17								
19	Leland Ave	LU-122	0.5 days	Wed 11/10/21	Wed 11/10/21	18								
20	Leland Ave	LU-123	1 day	Thu 11/11/21	Thu 11/11/21	19								
21	Leland Ave	LU-213	1 day	Fri 11/12/21	Fri 11/12/21	20								
22	Leland Ave	LU-214	1 day	Mon 11/15/21	Mon 11/15/21	21								
23	Leland Ave	LU-215	1 day	Tue 11/16/21	Tue 11/16/21	22								
24	Rutland Ave	LU-216	0.5 days	Wed 11/17/21	Wed 11/17/21	23								
25	Rutland Ave	LU-217	1 day	Wed 11/17/21	Thu 11/18/21	24								
26	Rutland Ave	LU-218	1 day	Thu 11/18/21	Fri 11/19/21	25								
27	Rutland Ave	LU-219	0.5 days	Fri 11/19/21	Fri 11/19/21	26								
28	Rutland Ave	LU-220	0.5 days	Mon 11/22/21	Mon 11/22/21	27								
29	Rutland Ave	LU-221	1 day	Mon 11/22/21	Tue 11/23/21	28								
30	Clifton Ave	LU-224	1 day	Tue 11/23/21	Wed 11/24/21	29								
31	Leigh Ave	LU-227	1 day	Wed 11/24/21	Thu 11/25/21	30								
32	Leigh Ave	LU-228	1 day	Thu 11/25/21	Fri 11/26/21	31								
33	Leigh Ave	LU-229	1 day	Fri 11/26/21	Mon 11/29/21	32								
34	Richmond Ave	LU-230	1 day	Mon 11/29/21	Tue 11/30/21	33								
35	Richmond Ave	LU-231	1 day	Tue 11/30/21	Wed 12/1/21	34								
36	Richmond Ave	LU-232	1 day	Wed 12/1/21	Thu 12/2/21	35								
37	Bascom/Laswell Easement	LU-112	0.5 days	Thu 12/2/21	Thu 12/2/21	36								
38	Bascom/Laswell Easement	HU-141	1 day	Fri 12/3/21	Fri 12/3/21	37								
39	Laswell/ Arieta Easement	LU-114	0.5 days	Mon 12/6/21	Mon 12/6/21	38								
40	Laswell/ Arieta Easement	LU-115	1 day	Mon 12/6/21	Tue 12/7/21	39								
41	Arieta/ Raymond Easement	LU-116	0.5 days	Tue 12/7/21	Tue 12/7/21	40								
42	Arieta/ Raymond Easement	LU-117	1 day	Wed 12/8/21	Wed 12/8/21	41								
43	Raymond/ Irving Easement	LU-118	0.5 days	Thu 12/9/21	Thu 12/9/21	42								
44	Raymond/ Irving Easement	LU-119	1 day	Thu 12/9/21	Fri 12/10/21	43								
45	Irving/ Leland Easement	LU-120	0.5 days	Fri 12/10/21	Fri 12/10/21	44								
46	Irving/ Leland Easement	LU-121	0.5 days	Mon 12/13/21	Mon 12/13/21	45								
47	Irving/ Leland Easement	LU-121A	0.5 days	Mon 12/13/21	Mon 12/13/21	46								
48	Cleveland Ave	LU-107A	1 day	Tue 12/14/21	Tue 12/14/21	47								
49	Cleveland Ave	LU-107	1 day	Wed 12/15/21	Wed 12/15/21	48								

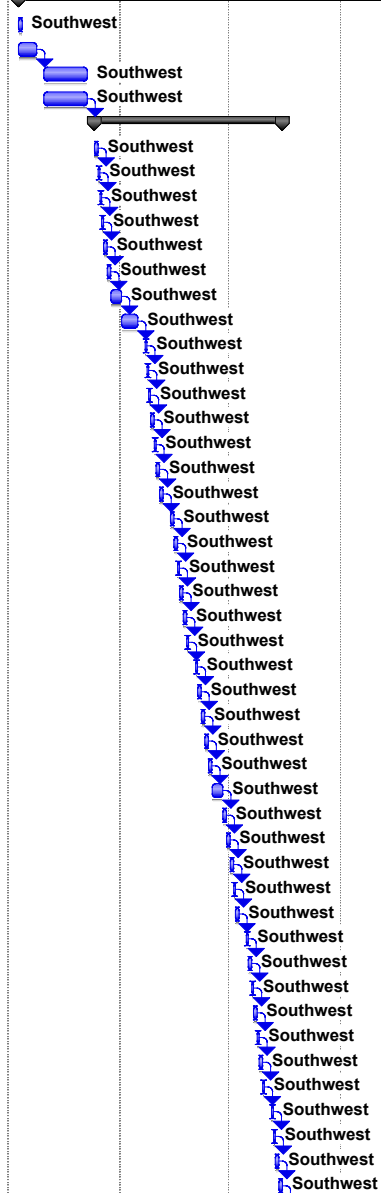

Project: Baseline Schedule - Burbank S
Date: Tue 9/28/21

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Burbank Sanitary District
Baseline Schedule

ID	Task Name	Pipe ID	Duration	Start	Finish	Predecessor	September	October	November	December	January	February	March	April
50	Post Video	-	5 days	Thu 12/16/21	Wed 12/22/21	49								
51	Install 62 LF of 4" PVC - 2349 Olive Ave.	LU-107	2 days	Mon 12/6/21	Tue 12/7/21									
52	Install New Property Line Cleanout - 2349 Olive Ave.	LU-107	1 day	Wed 12/8/21	Wed 12/8/21	51								
53	Point Repairs	-	30 days	Thu 12/9/21	Wed 1/19/22	52								
54	Bailey Ave.	LU-101	2 days	Thu 12/9/21	Fri 12/10/21									
55	Bailey Ave.	LU-102	4 days	Mon 12/13/21	Thu 12/16/21	54								
56	Boston Ave.	LU-109A	3 days	Fri 12/17/21	Tue 12/21/21	55								
57	Laswell Ave.	LU-201	4 days	Wed 12/22/21	Mon 12/27/21	56								
58	Laswell Ave.	LU-203	4 days	Tue 12/28/21	Fri 12/31/21	57								
59	Vaughn Ave.	LU-204	2 days	Mon 1/3/22	Tue 1/4/22	58								
60	Vaughn Ave.	LU-206	2 days	Wed 1/5/22	Thu 1/6/22	59								
61	Clifton Ave.	LU-223	2 days	Fri 1/7/22	Mon 1/10/22	60								
62	Clifton Ave.	LU-225	3 days	Tue 1/11/22	Thu 1/13/22	61								
63	Scott St.	HU-131	0.5 days	Fri 1/14/22	Fri 1/14/22	62								
64	Scott St.	HU-132	2 days	Fri 1/14/22	Tue 1/18/22	63								
65	Scott St.	HU-134	1 day	Tue 1/18/22	Wed 1/19/22	64								
66	Raymond Ave.	HU-140	0.5 days	Wed 1/19/22	Wed 1/19/22	65								
67	Project Close-out	-	32 days	Thu 1/20/22	Fri 3/4/22	66								

Project: Baseline Schedule - Burbank S
Date: Tue 9/28/21

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
